Predictive Analytics Program

Bid Proposal and Week 4 Progress Review

DataForge Consulting

Daniel Felipe Martínez Hernández · Rafael Alejandro Baracaldo Doikov · Oscar Santiago Merino Suárez
Escuela Colombiana de Ingeniería Julio Garavito — GMAC

September 2026

Client: FinBank S.A. — Vice Presidency of Risk and Analytics

What FinBank is losing today

$420,000M
Credit portfolio, 125,000 clients

$58,800M
Exposure with no early delinquency alerts

$18,200M
Losses from churn that was never anticipated

Total exposure: COP $77,000 million, close to 18% of the portfolio

The bank records delinquency after the payment is missed and cancellation after the client has left. Both numbers are the cost of finding out too late.

Our reading, and who we are

The obstacle is management, not statistics

FinBank has data and analysts. What is missing is a defined way to plan, control and close an analytical project: a scope, an owner for each decision, a cadence, and a rule to stop or continue.


DataForge Consulting

Daniel Martínez — Project Leader
Rafael Baracaldo — Business Analyst
Oscar Merino — Scrum Facilitator

How we protect your money

Six sprints, six reviews. At each one you see the monetary effect, the variance and the risks, and you authorize the next two weeks. Maximum committed between decisions: COP $30,000,000.

What we will build and how we will run it



PMBOK for control

Charter, scope, cost baseline, risk register and change control. This fixes what cannot move: 12 weeks and COP $180,000,000.

Scrum and Kanban for delivery

Two week sprints, a visible board with work in progress limits, and a Definition of Done that requires business approval, not only technical validation.

Monitoring plan includes a drift trigger: AUC or recall down more than 0.05 for 2 straight weeks flags the model for retraining.

Agile board and backlog

Trello board structure

Product Backlog · Ready · In Progress · Client Validation · Blocked · Done

- Every card has an owner, a due date and a task checklist
- Nothing reaches Done without business validation

Sample user stories

US-06: risk analyst wants a delinquency model at 30/60 days to rank new clients by default probability.

US-08: retention manager wants a churn model, 3-month horizon, to contact preferential clients before they cancel.

RACI · internal team

Activity	D	R	O
Charter, scope, budget	R	C	I
Data diagnosis, feature dict.	A	R	C
Model build & validation	A	R	C
Cost threshold (O3)	R	R	I
Deployment & monitoring	R	C	R
Sprint cadence, board, DoD	C	I	A/R

D=Daniel, R=Rafael, O=Oscar. Full 9-stakeholder RACI (Sponsor, DPO, Collections, Retention, IT, Finance) is in Charter Section 2.

10 user stories written, prioritized and estimated. Board link delivered with this proposal.

Roadmap and budget

Sprint	Weeks	Focus
S1	1–2	Governance, data access, board
S2	3–4	Profiling and feature dictionary
S3	5–6	Delinquency model, AUC ≥ 0.75
S4	7–8	Churn model, three months ahead
S5	9–10	Thresholds and operating rules
S6	11–12	Pilot, monitoring and handover

Cost item	COP
Management and governance	27,000,000
Data engineering	45,000,000
Predictive modeling	54,000,000
Validation and documentation	25,200,000
Pilot, training, handover	18,000,000
Contingency reserve	10,800,000
Total	180,000,000

Reserve discipline

The reserve belongs to no sprint. It is released by you, in a review, and only against a risk that has already materialized.

Risks we already know, and what we ask from you

ID	Risk	Exposure	Response
R1	Delay in data access	High	Condition to close Sprint 1, anonymized sample in parallel
R2	Incomplete client history	High	Quality report in Sprint 2 and documented exclusions
R3	Low event rate	Medium	Metrics suited to imbalance, thresholds set by monetary benefit
R4	Model not adopted	High	Business approval required inside the Definition of Done
R5	Data protection	Medium	Anonymization before extraction and legal review
R6	Scope growth	Medium	Sprint backlog fixed once the sprint has started

What we ask from FinBank

36 months of credit history in week 1, two hours per week from collections and retention, and a sponsor present at the six reviews.

What you own at week 12

Two validated models, the operating rules, the board, the monitoring plan and analysts trained to run it.

Progress Review — Week 4

End of Sprint 2 · Agile execution and Kanban board · Gate 2 decision

Where we are: end of Sprint 2

4 of 12

Weeks elapsed. One of six milestones closed, the second due this sprint

$54.8M

Spent against COP $56.4M planned

1

Active impediment, open for 4 days


Closed in Sprint 1

Charter approved, data access agreement signed under Ley 1581, product backlog with all ten user stories, board and Definition of Done in operation.


Committed for Sprint 2

Data quality report, feature dictionary version 1, business validation of variables, and the delinquency target definition at 30 and 60 days.

Our Kanban board today

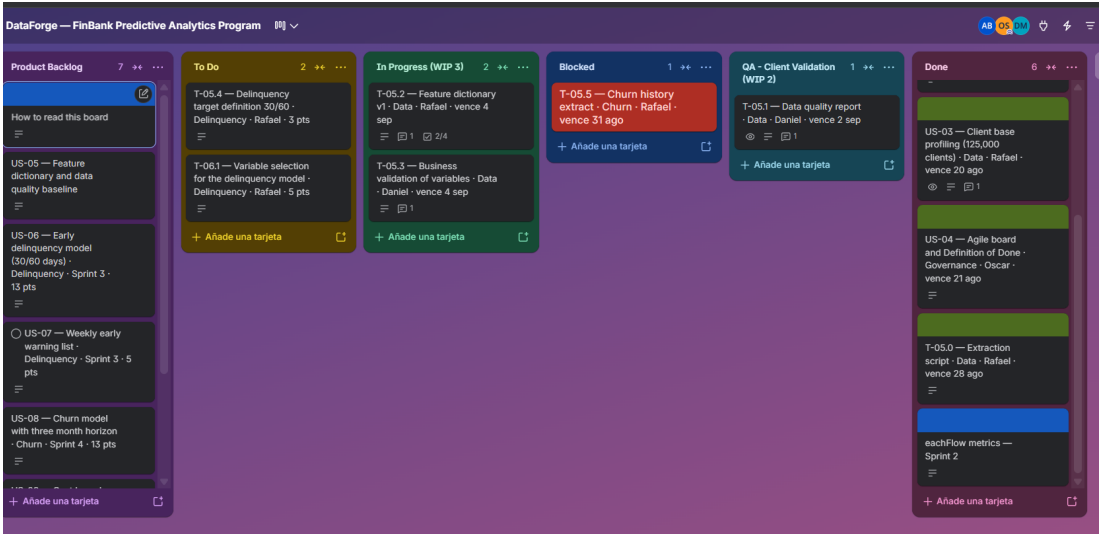

What the board tells us

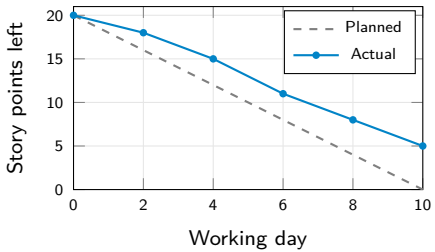

Flow metrics

- Throughput: 4 cards in Sprint 1, 3 so far in Sprint 2
- Average cycle time: 3.2 days
- Work in progress limit respected in 9 of 10 days
- 5 of 20 points will not close in this sprint

Reading

The gap is not productivity. It is one blocked card that carries 5 points and cannot advance without external data.

The impediment and what we did with it

R1 has materialized, in part

The churn history extract requires a credential from the IT area that has been pending for four days. Delinquency data arrived complete; churn data did not.

Actions already taken

- Card moved to Blocked on day 6 with the cause written on it
- Outside what R1's own mitigation plan covers, so escalated to the sponsor on day 7 through change control
- Work reordered: the delinquency target definition was pulled forward

What we ask in this review

- Escalation of the credential with the IT director this week
- Release of COP $4,200,000 from the reserve only if the block passes ten days, to contract the extraction externally

Gate 2: the decision we need from you

Status of the engagement

- Schedule: milestone M2 slips into Sprint 3, 5 points carried over
- Cost: COP $54.8M spent against $56.4M planned, variance below 3%, inside our 5% ceiling
- Risks: R1 partially materialized, R2 closed, R4 on track (business owner in every review), R5 on track

Proposal for Sprint 3

- Start the delinquency model with the 18 variables already validated
- Keep churn on hold until the extract is released, without moving milestone M4
- Carry the 5 blocked points into Sprint 3

Continue, redirect or stop. The board is on the table and the decision is yours.

DataForge Consulting — Thank you. Questions?
